



# Huntington Beach City School District


---



- 1. Where are we in the process?**
- 2. Measure Q Bond Program Updates**
- 3. District Wide Priorities**
- 4. Measure Q Phasing by Priority**
- 5. Campus Projects & Phasing**
- 6. Schedule**
- 7. Phase 1 Schematic Design**

# Where are we in the process?

---



- 1. Project Prioritization Site Meetings** January 10-11, 2017
  - BCA's team held site meetings to review the Bond Program planned projects for each campus.
- 2. Project Prioritization Board Presentation** January 17, 2017
  - BCA's team presented the overall project prioritization for the Measure Q Bond Program.
- 3. Demonstration Classroom Teacher Meeting** March 28, 2017
  - OnPoint presented the designs for each of the (12) demonstration classrooms.
- 4. Phase 1 Schematic Design (SD) Phase** April 17, 2017
  - BCA began the SD phase for the phase 1 projects.
- 5. Schematic Design (SD) Site Committee Meetings** May 3 - 5, 2017
  - BCA's team will meet with each campus site committee to review the SD phase scope/designs for phase 1 projects.
- 6. Schematic Design (SD) Board Presentation** May 16, 2017
  - BCA's team will present the final SD phase scope/designs for phase 1 projects.



**Priority 1:** 21st Century Classrooms and upgrades to portables, AB300 [DSA will require it to be in this phase], ADA, electrical gear/service upgrades, abatement, restroom and ADA upgrades, roof replacement, plaster repair at Dwyer.

**Priority 2:** Multipurpose and STEAM Labs at the [2] Middle Schools, LED lighting and lighting controls, air conditioning and controls, new playground at Smith, Admin. rework, replace concealed spline ceilings at Sowers, upgrade Auditorium at Dwyer.

**Priority 3:** Learning Commons.

**Priority 4:** Safety and security single point of entry/exit at Admin., site fencing, remove/modify walkway canopies, restrict roof access, and portables to permanent.



**Phase 1** (Priority 1 & 2) **2017-2020** (3 years)

**Phase 2** (Priority 1 & 2) **2020-2023** (3 years)

**Phase 3** (Priority 2 & 3) **2023-2026** (3 years)

**Phase 4** (Priority 3 & 4) **2026-2029** (3 years)

---

**Measure Q Bond Program** **2017-2029** (12 years)



<b>2017-2020 Phase 1:</b>	<b>\$50,000,000</b> (initial projection \$57M)
2020-2023 Phase 2:	\$49,850,000 (initial projection \$53M)
2023-2026 Phase 3:	\$30,000,000 (initial projection \$13.85M)
<u>2026-2029 Phase 4:</u>	<u>\$30,000,000</u> (initial projection \$36M)
<b>2017-2029 TOTAL:</b>	<b>\$159,850,000</b>

- Complete (1) demonstration classroom at each campus during the 2017 summer.
- Complete all life safety projects in the first phase.
- Complete new Middle School STEM labs and gym/multi-purpose projects in the first phase to allow all HBCSD students to engage in these state of the art environments as quickly as possible.
- Complete 21<sup>st</sup> century classroom renovations District wide in the first two phases.

# Measure Q Bond Projects PERRY ELEMENTARY SCHOOL



Perry Elementary School - Measure Q Bond Projects	Phase 1 (2017-2020)	Phase 2 (2020-2023)	Phase 3 (2023-2026)	Phase 4 (2026-2029)
(1) Demonstration Classroom	\$ 85,000			
Replace Hardscape		\$ 300,000		
Replace windows		\$ 150,000		
21st Century Classroom Renovations		\$ 4,000,000		
21st Century Portable Renovations		\$ 200,000		
New Electrical to Admin. and Multi-purpose		\$ 500,000		
Administration Renovation		\$ 500,000		
Library to Learning Commons Renovation		\$ 75,000		
Subtotal	\$ 85,000	\$ 5,725,000	\$ -	\$ -
Contingency (10%)	\$ 8,500	\$ 572,500	\$ -	\$ -
Construction Escalation (4% per year)	\$ -	\$ 1,007,600	\$ -	\$ -
<b>TOTAL ESTIMATED HARD CONSTRUCTION COST</b>	<b>\$ 93,500</b>	<b>\$ 7,305,100</b>	<b>\$ -</b>	<b>\$ -</b>

\*The estimates above are conceptual budget estimates – project cost will be refined after further analysis





## Phase 1 Projects (2017 - 2020)

- **Demonstration Classroom – Room 8 (Title 1 / STEM) - Estimated Completion Fall 2017**

## Phase 2 Projects (2020 - 2023)


- **Replace Hardscape**
- **Replace Windows**
- **21<sup>st</sup> Century Classroom Renovations**
- **21<sup>st</sup> Century Portable Classroom Renovations**
- **Administration Renovation**
- **Library to Learning Commons Renovation, Replace Windows**
- **New Electrical to Admin & Multi-purpose**

## Phase 3 Projects (2023 - 2026)

- **No Work**

## Phase 4 Projects (2026 - 2029)

- **No Work**



**Design**

**Feb 17 – April 17**

**FF&E Procurement**

**April 17 – June 17**

**Construction**

**June 17 – Aug 17**

**Occupancy**

**Fall 2017**

**Training & Evaluation**

**Sept 17 – Dec 17**

**Finalize Phase 1 FF&E**

**Dec 17 – Jan 18**


# Demo Classroom

Perry Elementary School Phase 1 Schematic Design



## PROJECT SCOPE:

- **New agile Student & Teacher Furniture**
- **New Student Devices & Charging Carts**
- **New Classroom Technology**
- **New Agile Classroom Storage**
- **New Carpet & Wall Finishes**

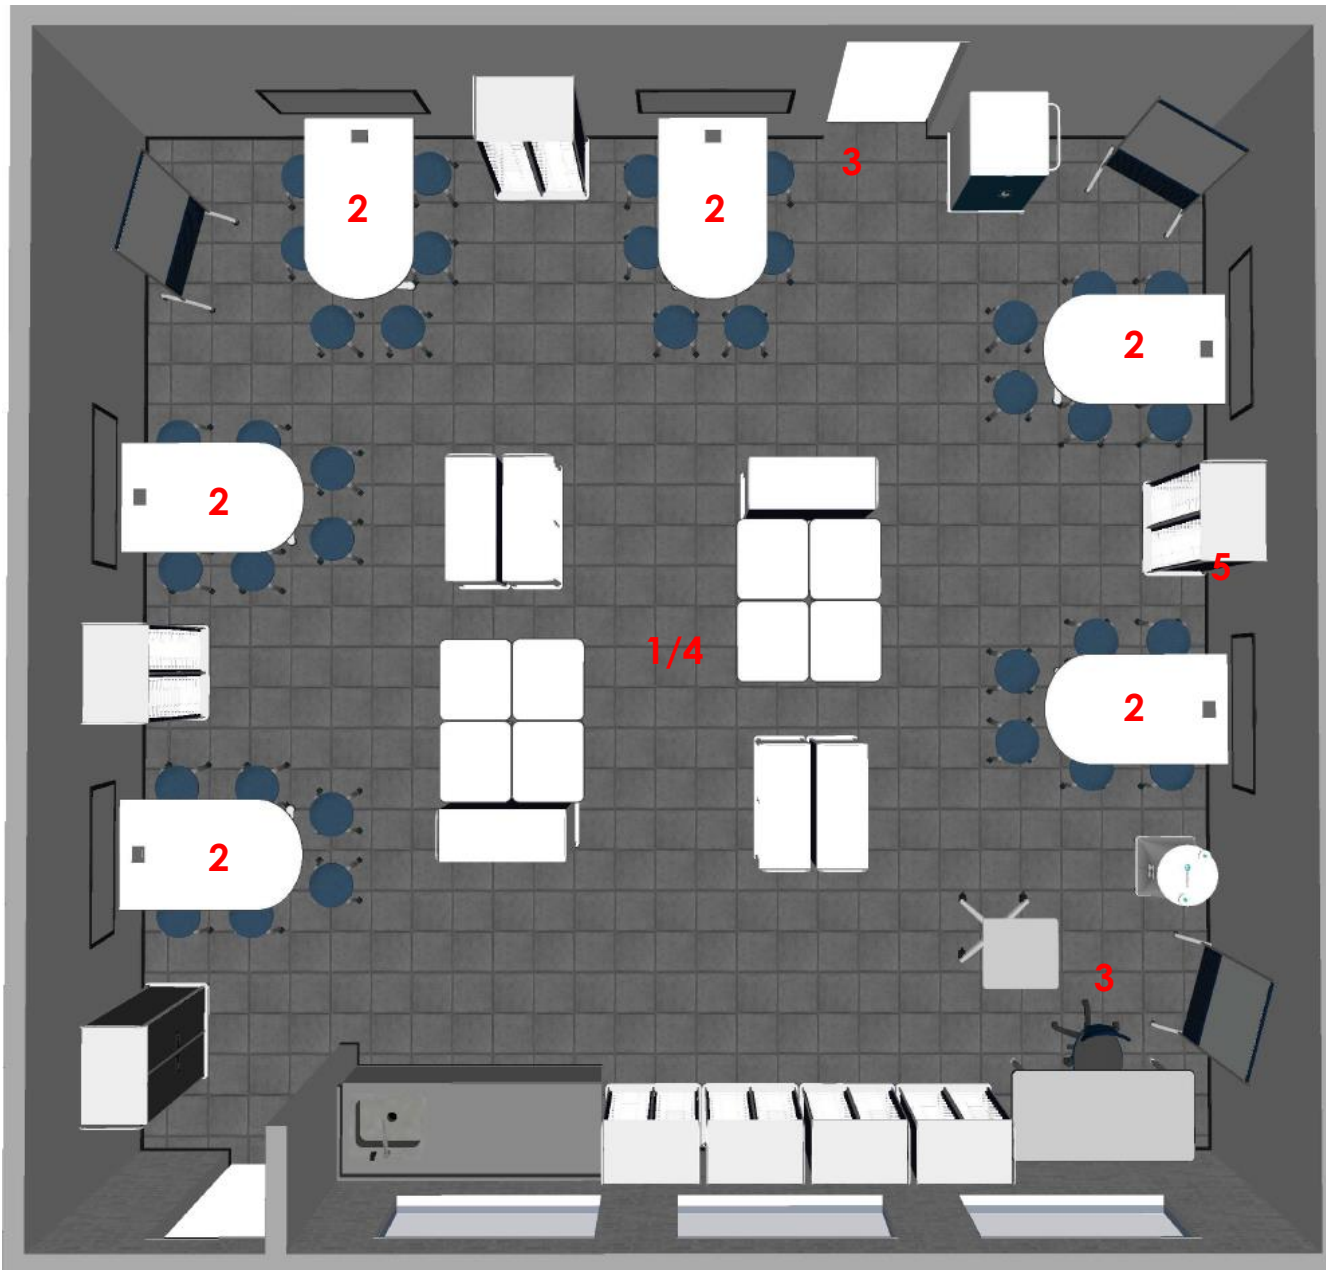

## Legend

1. Instruction Space
2. Lab Space
3. Teacher Space
4. Discovery Space

## Amenities

- Interactive Projector
- LCD Flat Screen
- Custom AV Control
- Agile Furniture
- Mobile Storage
- 1:1 Student Devices
- Charging Carts
- New Carpet
- Window Tinting
- LED Lighting

# Q & A



**Seamus O'Connor,** [seamuso@bcaarchitects.com](mailto:seamuso@bcaarchitects.com)  
Associate / Project Manager

