



Huntington Beach City School District



Board Meeting Presentation – Sowers Middle School

June 13, 2023

Agenda



A. Sowers MS Update

1. Construction Phase Progress
2. Schedule Update



Sowers MS Update



1. Construction Phase Progress

- Underground utility and infrastructure installation is ongoing – Edison vault installed on site with connections to location of new transformer.
- Building slab for Administration Building 100 has been poured over grade beams
- Formwork for stage area of Building 100 in progress



Sowers MS Update



1. Construction Phase Progress


- AMS Buildings – Factory production is complete, scheduling for site installation ongoing
- Trenching for Building 800 grade beams, Building 600 rebar layout, Building 500 grade beam pouring all in progress.
- Installation of underground drainage for AMS building in progress



Status of Sowers Middle School Project



2. Schedule Update – Phase 1

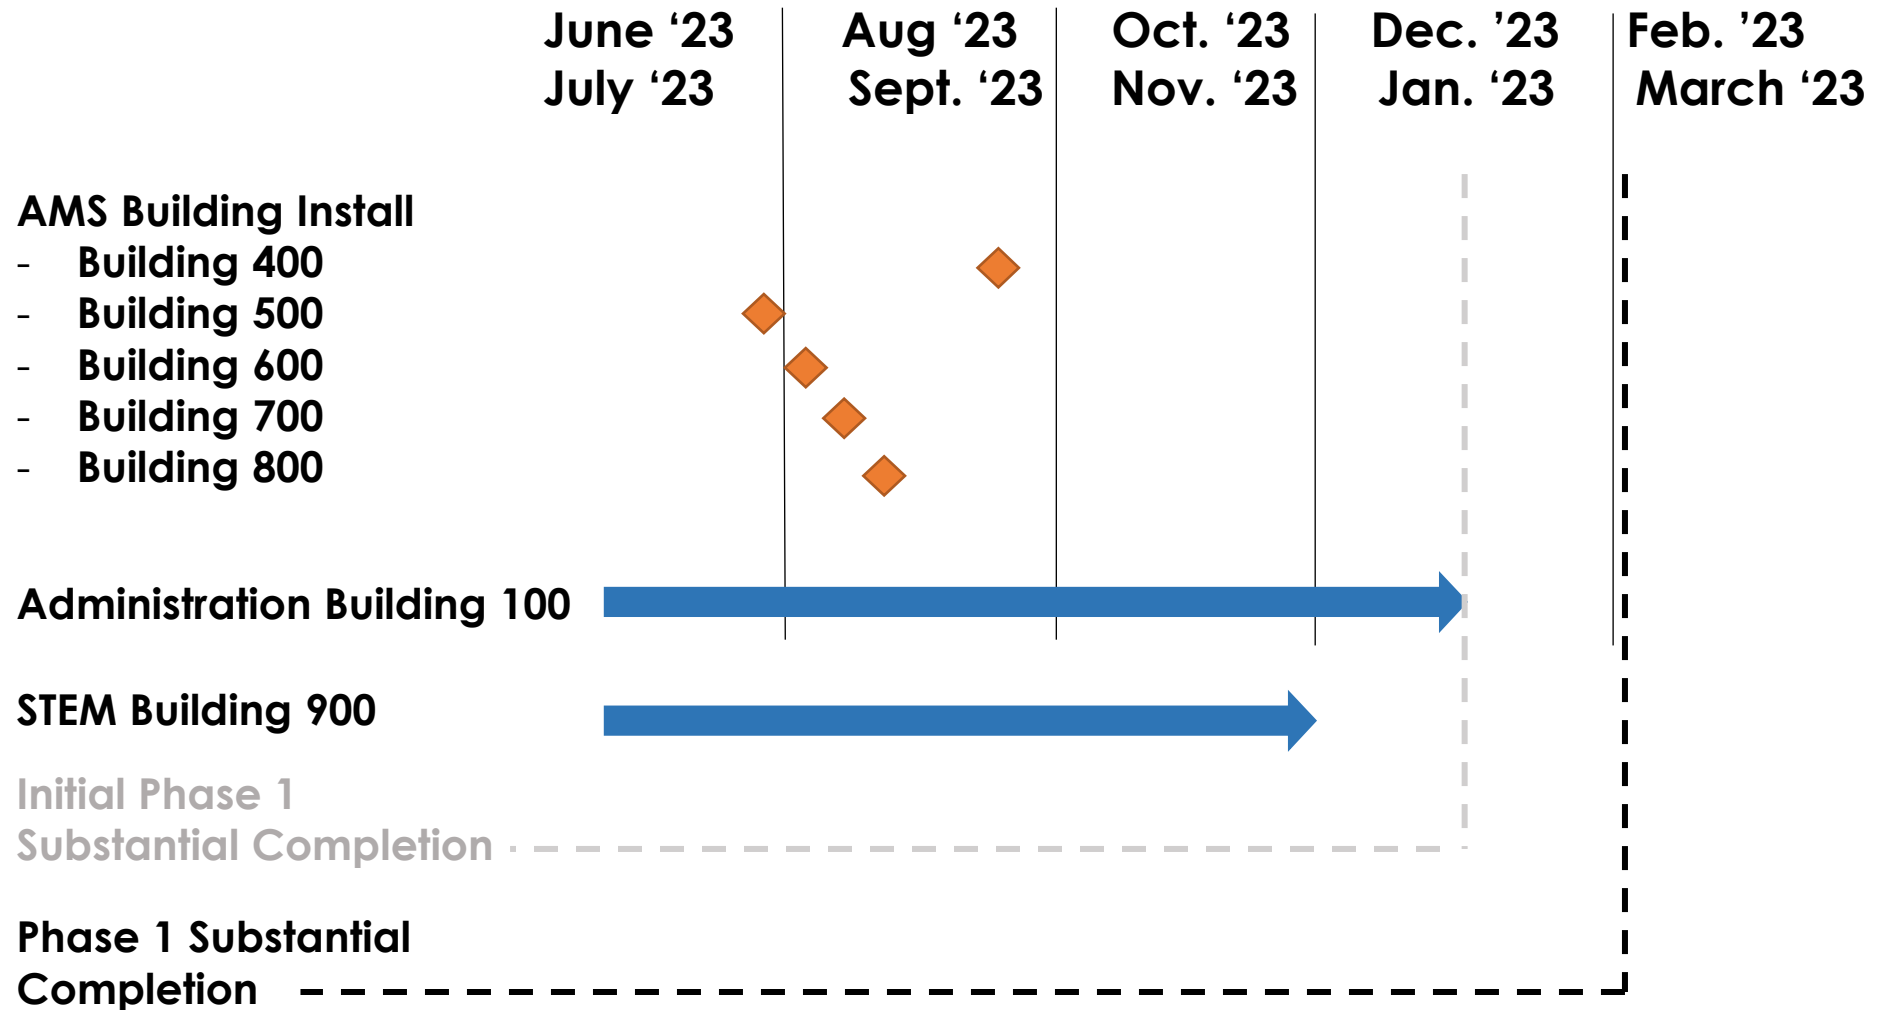

Q & A



Tony Pacheco Taylor, AIA, LEED tonyp@studiow-architects.com 949-880-7230
Client Leader, Associate – Studio W Architects
